


Setup Number 14	Survey Date 22-Mar-2004	Road Name 9332 Crosby	Direction Downstream
Facility	Van Reference	Place Name Garden Grove	
Work Order Number	Van operator JMS	Comments	
Cassette Num 026	Weather		

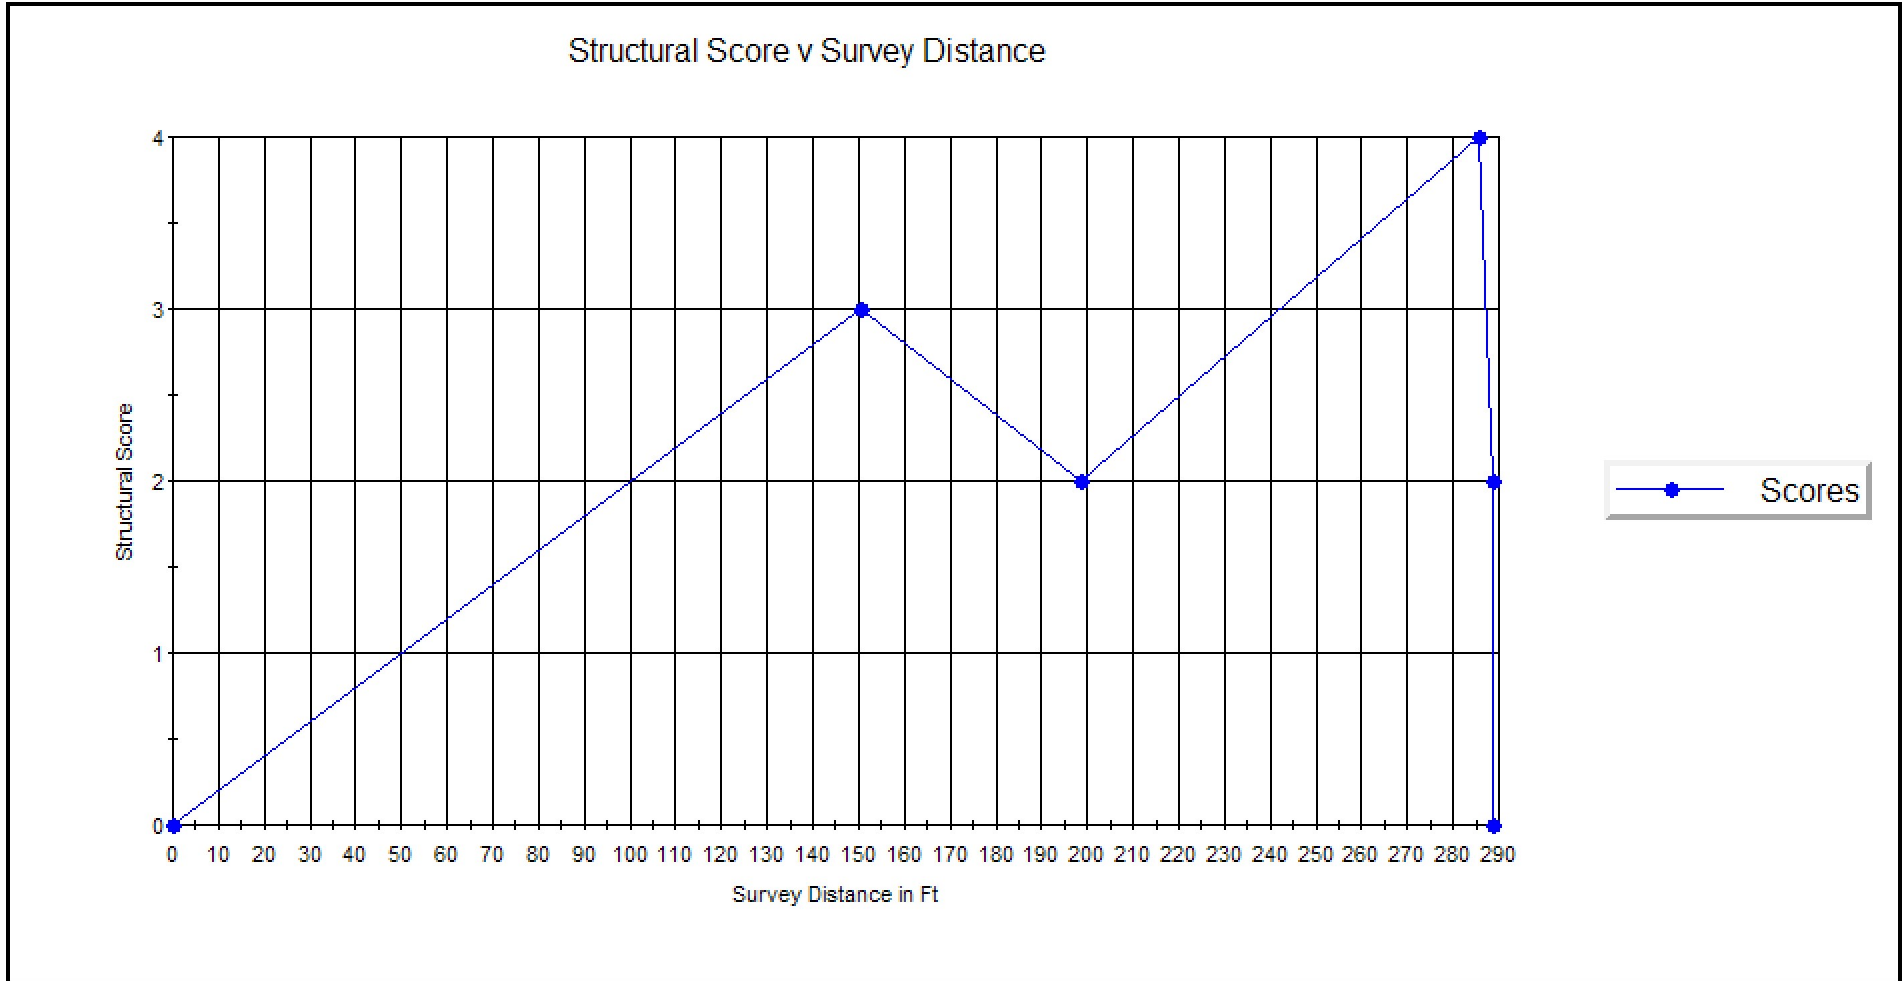

Start MHM130044
Cover level Ft
Depth Ft
Invert Level Ft

Pipe shape Circular
Material Vitrified Clay Pipe
Lining
Pre-clean J
Total Score 11 **Peak Score** 4 at 286 Ft

Size 8 **By** ins
Joint Spacing 03.00 Ft
Scheduled length 308.0 Ft
Year laid
ICG 2 **SPG**

Finish MHL130015
Cover level Ft
Depth Ft
Invert Level Ft

